


<b>Inspection Certification</b>	1196	
<b>Article</b>	Spreader bare light	
<b>Customer</b>	SupAir	
<b>Testlocation - Date</b>	05.05.12	
<b>Temp. C°/ humidity</b>	20,5 - 45,6%	
<b>Inspectors - No.</b>	Guido Reusch	
<b>Chart start at [N]</b>	10 daN	
<b>Limit value [N]</b>	220 daN	→ 19800,0 N (• Lv)
<b>Loadfactor Lv [g]</b>	9,0 g	
<b>rating unit (InpFile)</b>	1000 N	
<b>Description/Norm</b>	LTF 91/09	

Results		
Overstepping the limit value for a time of	<b>18,7</b>	<b>Sek.</b>
Chart start at	9,8	Messzeit (- 1 Sek.)
Chart end at	111,2	Messzeit (+ 1 Sek.)
Maxima > F <sub>p</sub>	2	
Maximum tensile load	20291	N
Comment	<b>passed</b>	

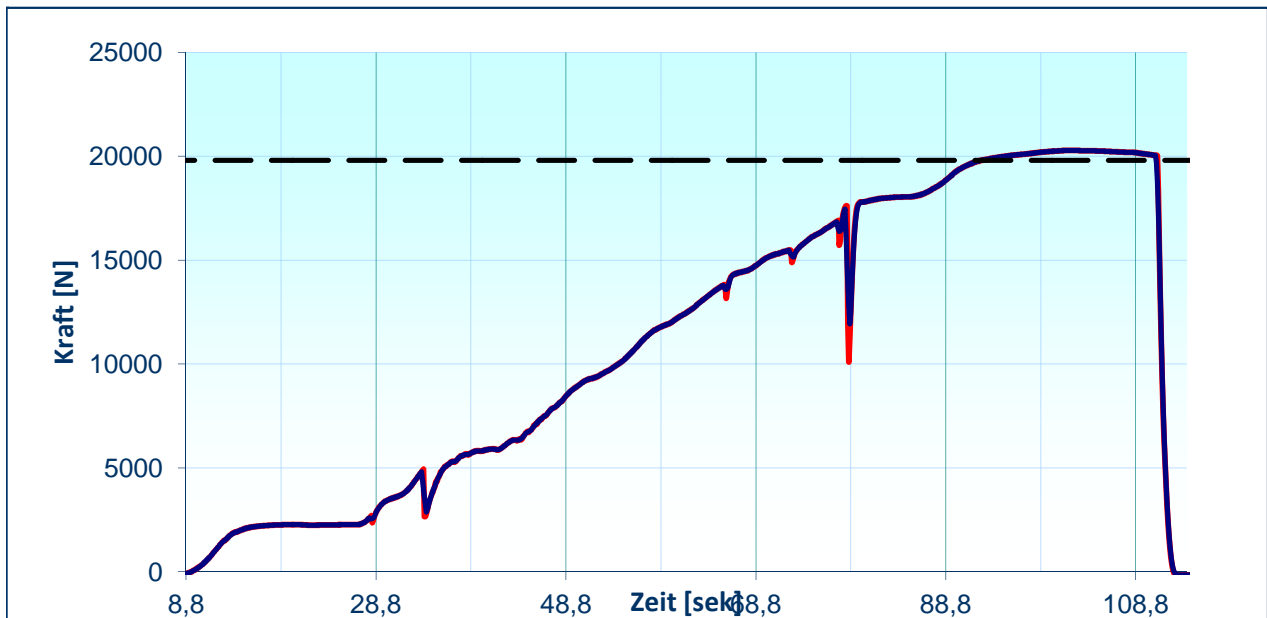

Bad Grönenbach,  
Ort, Datum

Prüfer

